

5 YR LRMP RECOMENDATION FORM

FAC. NO# *RR-9*


DATE INSPECTED

6-11-87

DESCRIPTION		YR 1	YR 2	YR 3	YR 4	YR 5
PAINT	INT			<i>12,000</i>		
	EXT			<i>4,000</i>		
ROOF						
STRUCT.	INT			<i>197,000</i>		
	EXT			<i>24,000</i>		
ELECTRICAL				<i>94,000</i>		
HVAC	HEAT			<i>294,000</i>		
	A/C					
MECH.	STM.					
	COND.					
	WATER					
	WASTE					
	OTHER					
TOTALS				<i>625,000</i>		

REMARKS
UNDER
EACH
YEAR

*LE 013M
FY. 90
INT/EXT
RENOVATION*

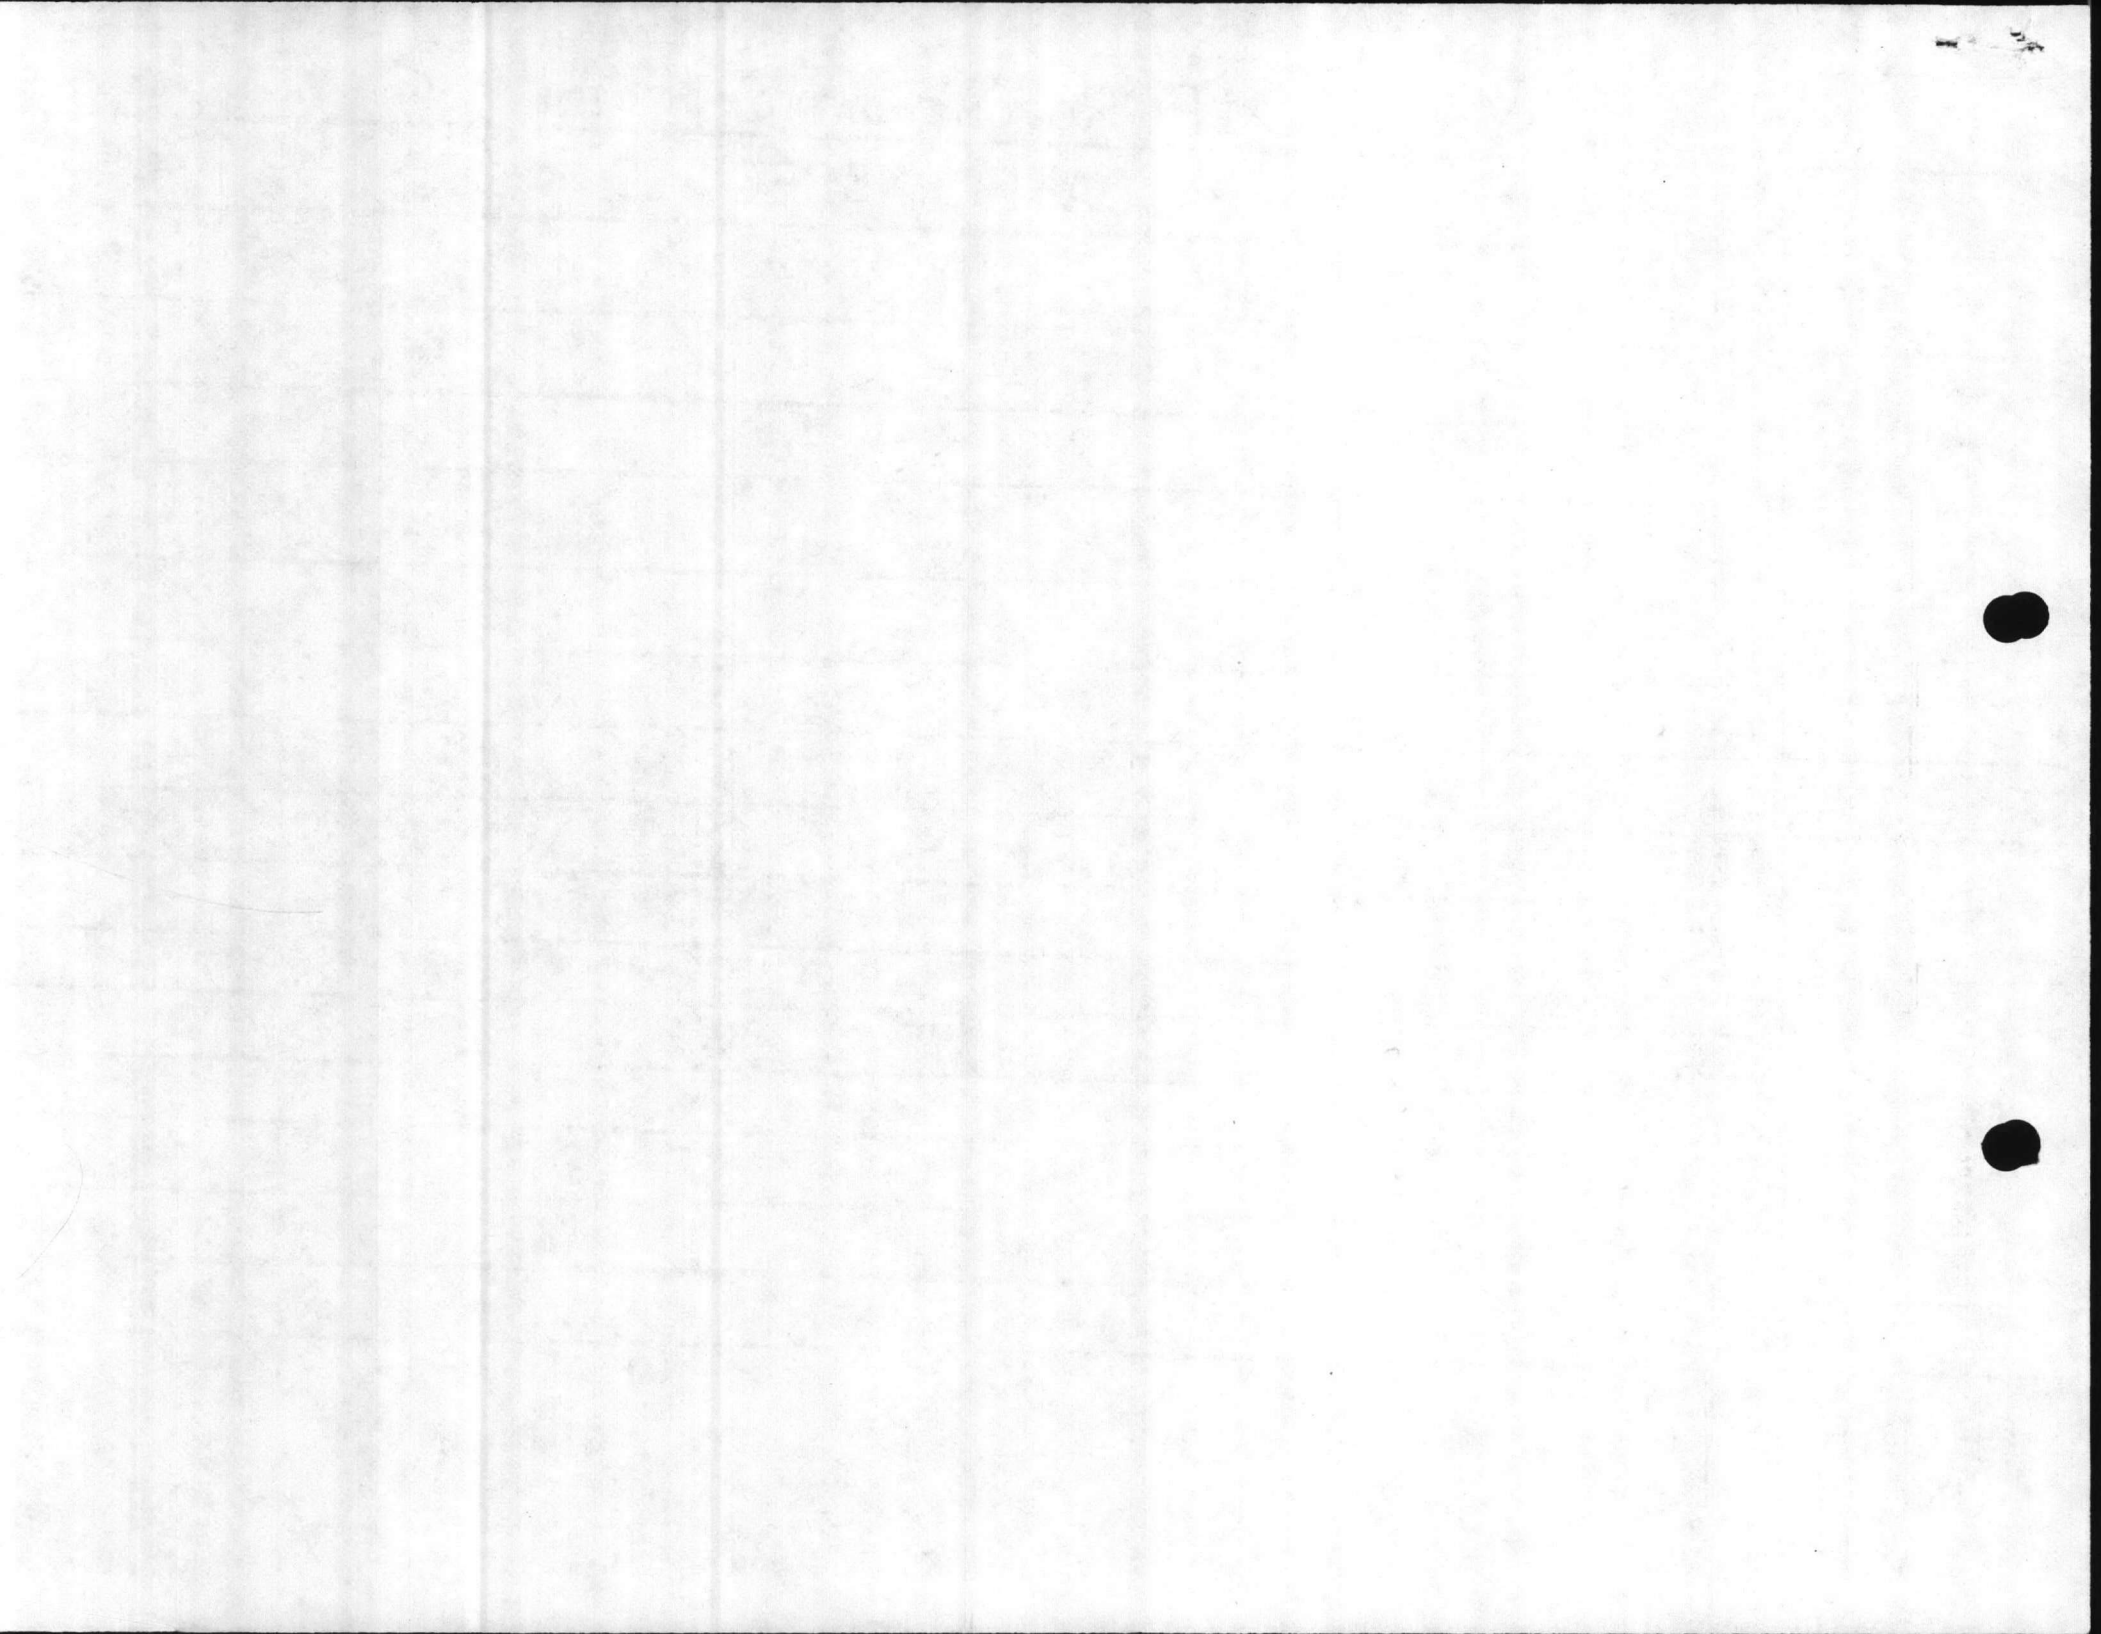

FACILITIES CONTROL INSPECTION REPORT

MCBCL 11100/1

Facility No. <i>RR-9</i>	Category Code <i>72411</i>	Facility: <i>UEP. E-1-E-4</i>	Date: <i>6-11-87</i>
		Inspector: <i>B. LANTIER</i>	

Map Coordinates	Description of Deficiencies	W	Labor	Labor	Mat.	Total
Page <i>16</i> of <i>90</i>		C	Hours	Cost	Cost	


EXTERIOR


Roof	<i>EXT. PT. 86-5433</i> <i>LEDISM. FY 90</i> <i>INT/EXT RENOVATION</i>					
Paint						
Doors						
Windows						
Walls						
Facia						
Soffit						

INTERIOR

Paint	<i>INT PT- 86-5433</i>					
Doors						
Windows						
Ceiling						
Walls						
Walls						
Walls						
Walls						

	Yes	No	Additional Inspection Reports
Electrical			
Mechanical			

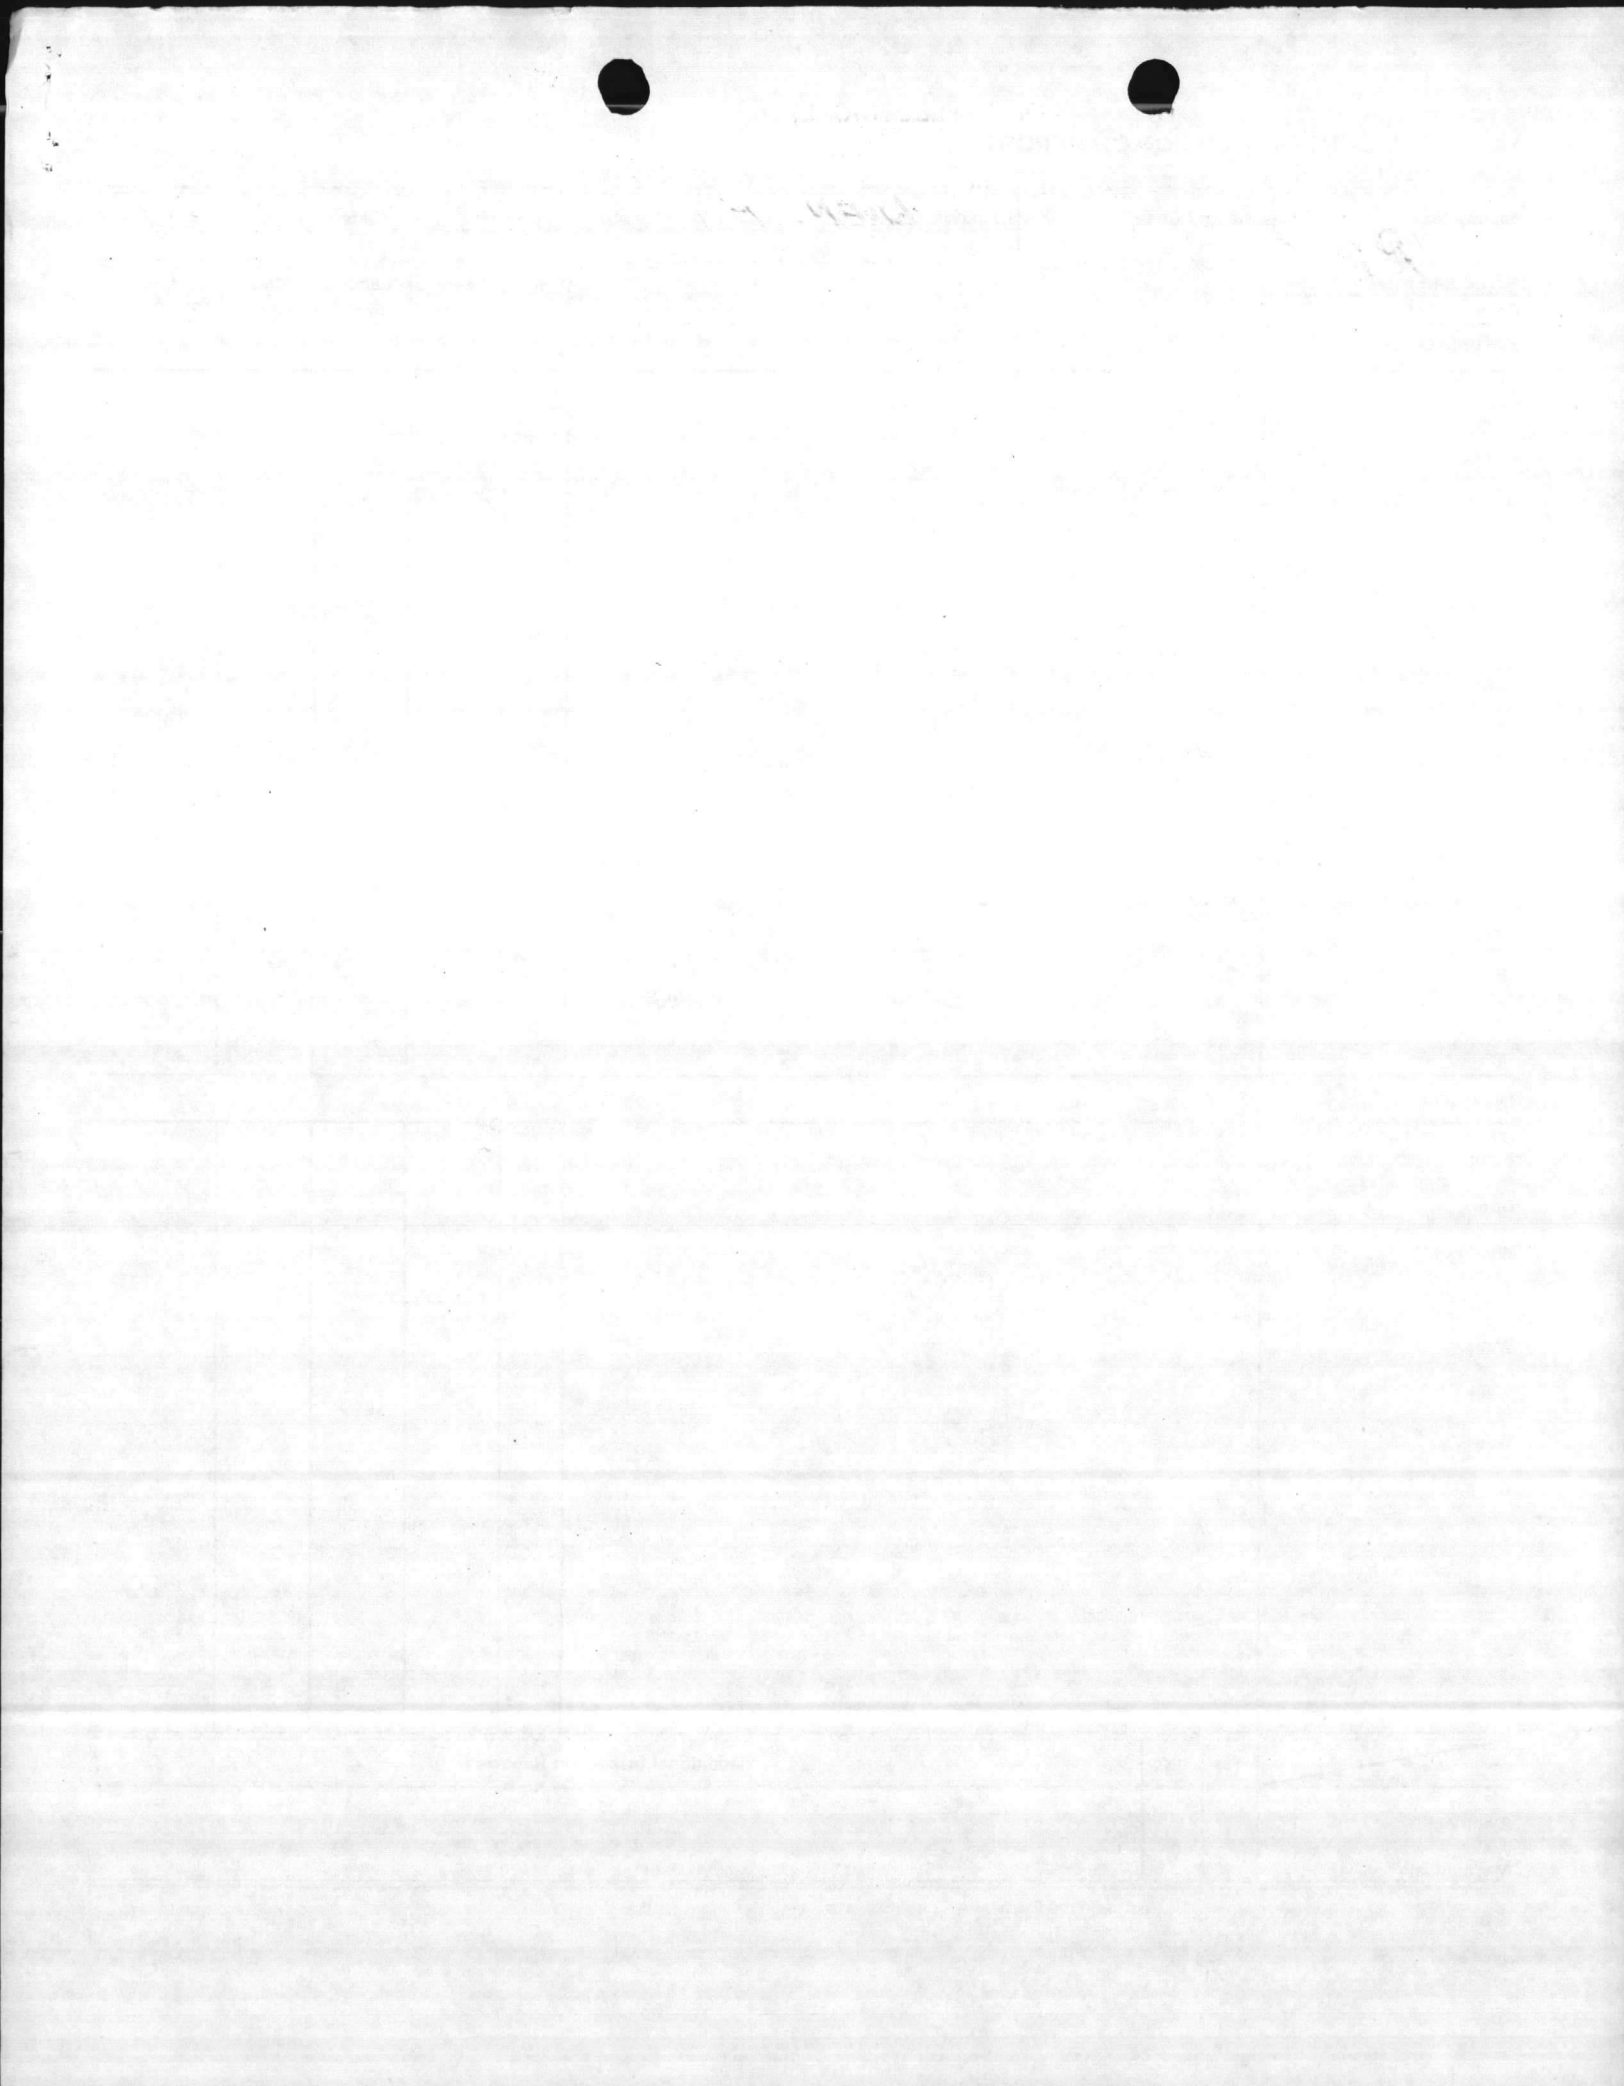

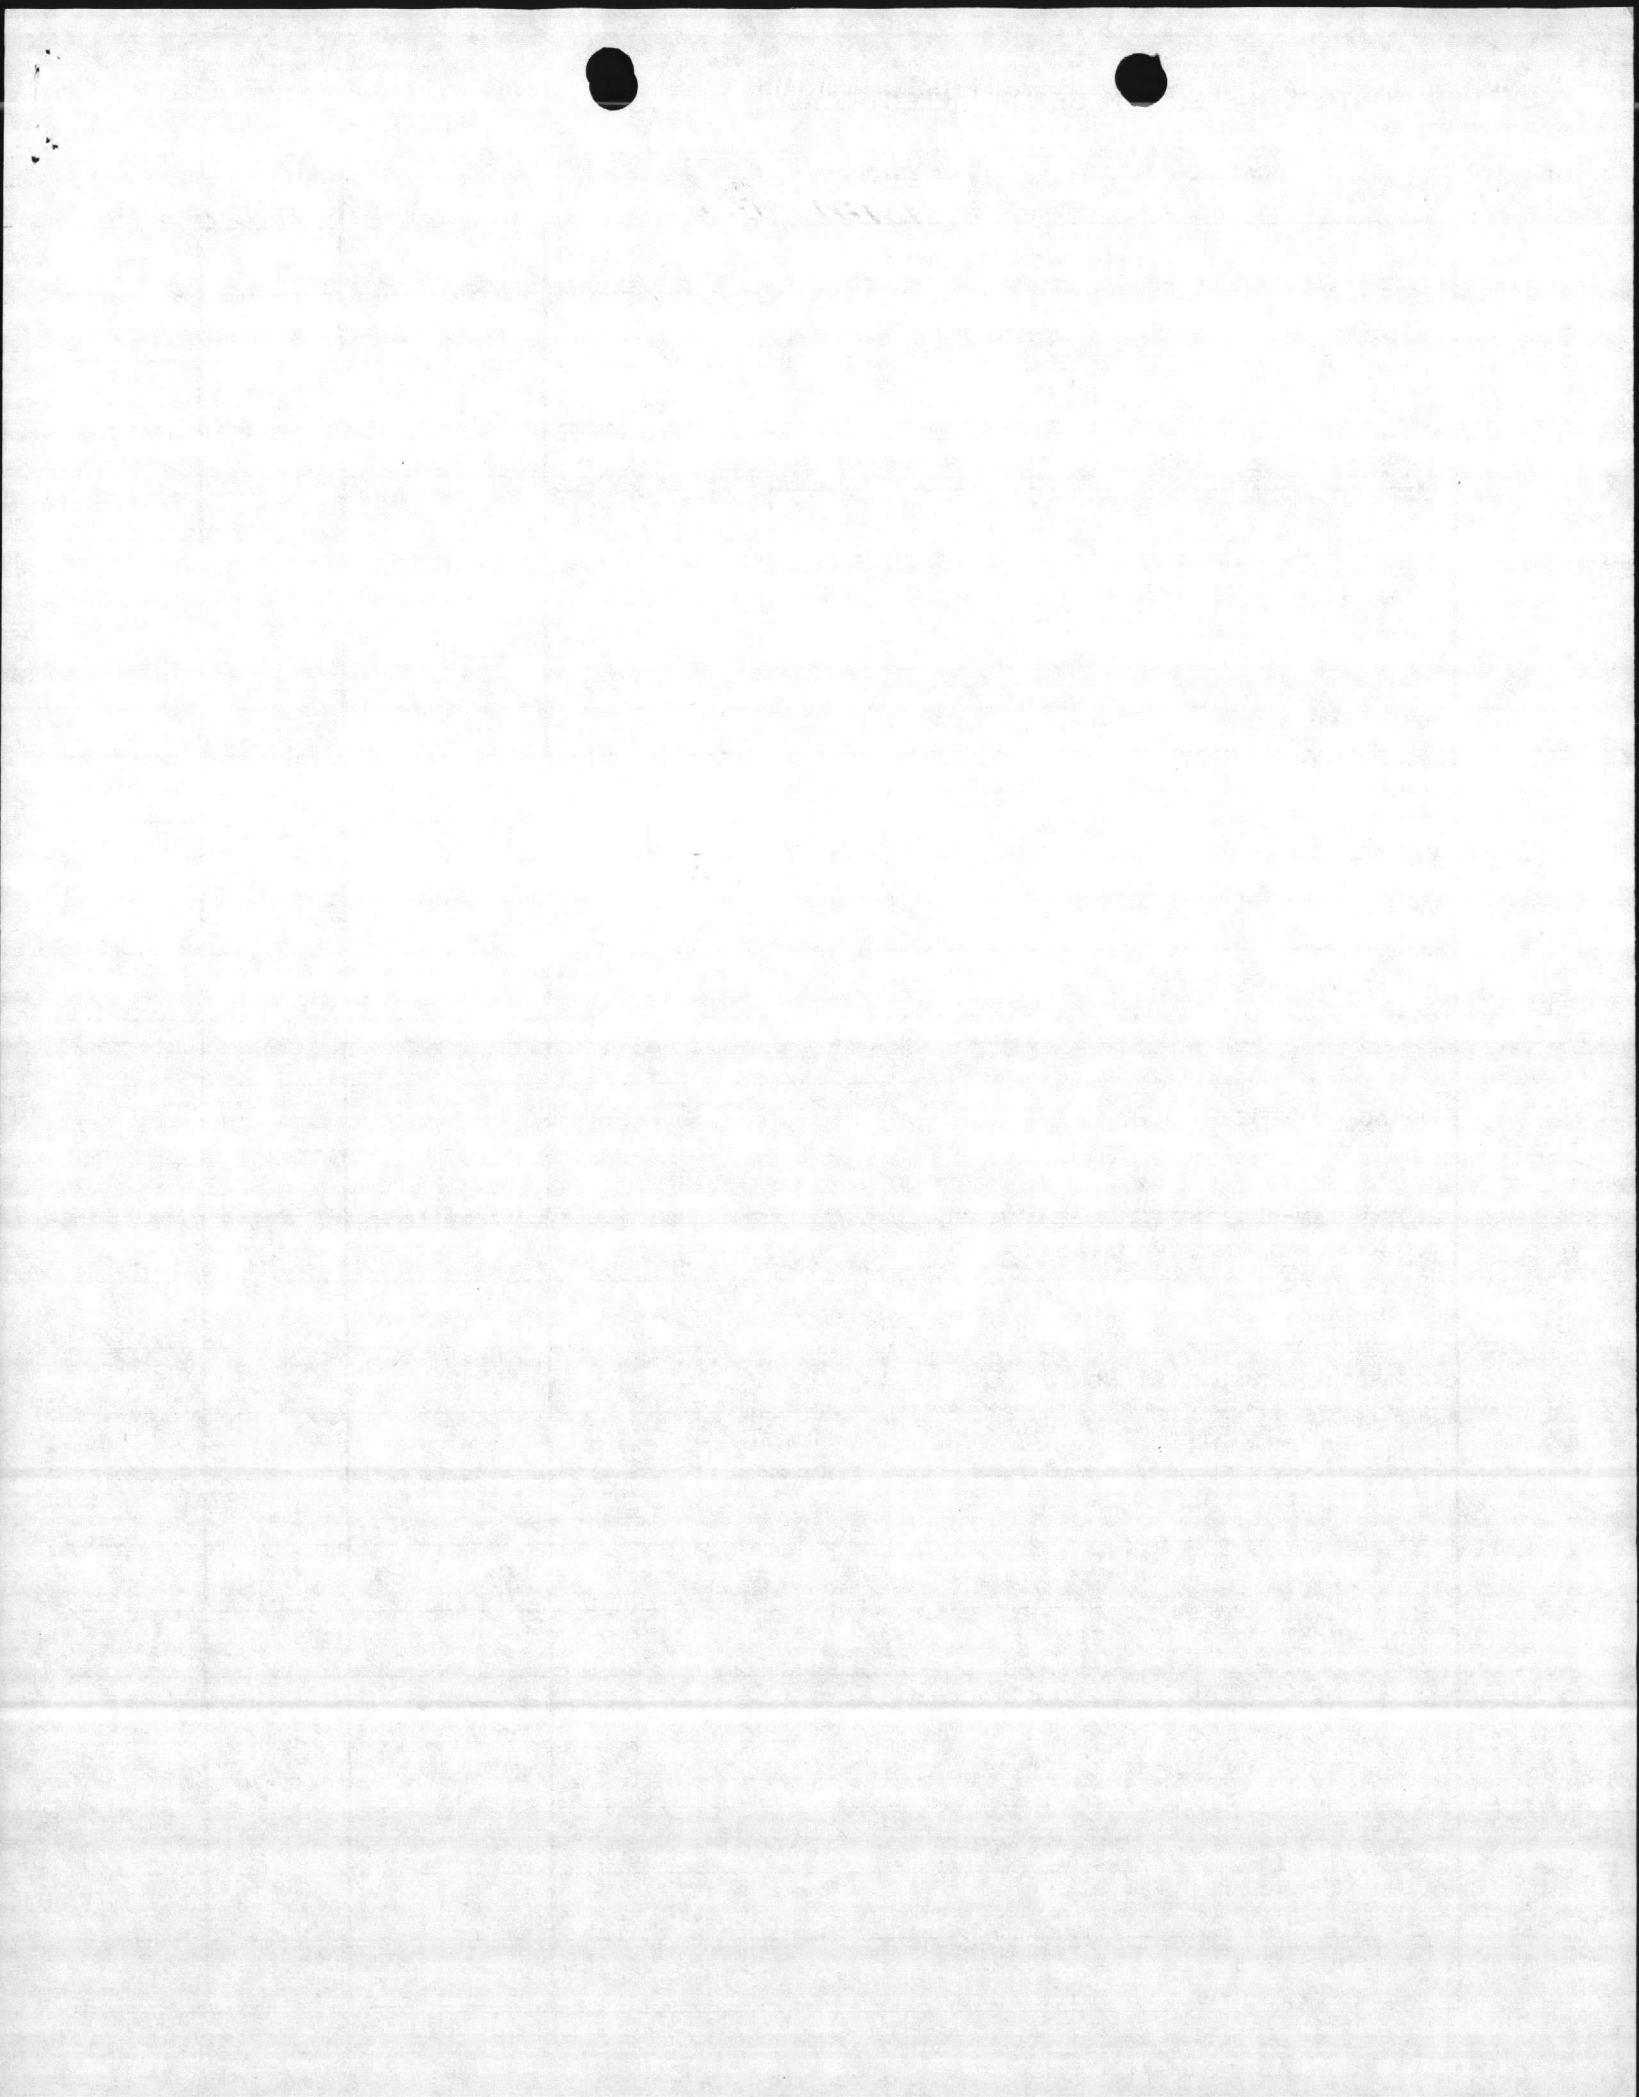

FACILITIES CONTROL INSPECTION REPORT (MECHANICAL)
 MCBCL 11100/3

FACILITY NO. RR-9 CATEGORY CODE 72411 INSPECTOR BLANTON DATE 6-11-87

WC	DEFICIENCY DESCRIPTION	HR	LBR \$	MAT \$	TOTAL
62	Replace condensate return lines throughout building				
62	Replace steam lines throughout building				
62	Replace piping in pit - Steam Reducing Station				
62	Replace reducing valve, temperature regulator valve				
62	Replace radiator, heating coil, unit heater <u>JO. 3303-RCPL</u>				
62	Replace hot water tank, instantaneous hot water heater <u>SHOWER STALL</u>				
61	Replace commode, urinal, lavatory, deep sink <u>LEOISM-FY-90</u>				
61	Replace shower stall, mixing valves, spigot <u>INT/EXT RENOVATION</u>				
61	Replace stand trap, floor drain concrete deck				
61	Replace "P" trap, supply line, supply valve				
61	Replace sewer line, hot water line, cold water line				
62	Replace insulation, steam line, hot water line, cold line				
53	Replace cooling tower with package air conditioning unit				
53	Replace air conditioning compressor, condenser/coil				
	<u>Asbestos on Cold & Hot Water LINES.</u>				

