

Kids.gov Redesign project schedule

ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
0		Kids.gov Redesign project schedule	156 days	Mon 11/14/11	Mon 6/18/12			100%
1		Project Management	110 days	Mon 11/14/11	Fri 4/13/12			100%
2		Develop high level project schedule	45 days	Mon 11/14/11	Fri 1/13/12			100%
3		Develop detailed schedule	65 days	Mon 1/16/12	Fri 4/13/12	2		100%
4		Requirements development	30 days	Mon 11/14/11	Fri 12/23/11			100%
5		Content analysis	14 days	Mon 11/14/11	Thu 12/1/11			100%
6		Generate Access report with current content	5 days	Mon 11/14/11	Fri 11/18/11			100%
7		Review report and compare against Cari's wireframes to determine gaps to be filled in	9 days	Mon 11/21/11	Thu 12/1/11	6		100%
8		Develop requirements	30 days	Mon 11/14/11	Fri 12/23/11	7FF		100%
9		CMS Selection	82 days	Mon 11/14/11	Tue 3/6/12			100%
10		Perform technical review of CM 1	20 days	Mon 11/14/11	Fri 12/9/11			100%
11		Review CM 1 against requirements	10 days	Mon 12/26/11	Fri 1/6/12	4		100%
12		Evaluate CM 1 demo	25 days	Mon 12/12/11	Fri 1/13/12	10		100%
13		Contractual modifications to acquire CM 1	37 days	Mon 1/16/12	Tue 3/6/12	10,11,12		100%
14		Website Design	90 days	Fri 12/2/11	Thu 4/5/12			100%
15		Wireframe development	35 days	Fri 12/2/11	Thu 1/19/12	5		100%
16		Design Kids/Teens wireframe	30 days	Fri 12/2/11	Thu 1/12/12			100%
17		Design Grown Ups wireframe	5 days	Fri 1/13/12	Thu 1/19/12	16		100%
18		Design development	55 days	Fri 1/20/12	Thu 4/5/12	15		100%
19		Design iteration 1	25 days	Fri 1/20/12	Thu 2/23/12			100%
20		Design Kids section	18 days	Fri 1/20/12	Tue 2/14/12			100%
21		Design Teens section	3 days	Wed 2/15/12	Fri 2/17/12	20		100%
22		Design Grown Ups section	3 days	Mon 2/20/12	Wed 2/22/12	21		100%
23		Management review	1 day	Thu 2/23/12	Thu 2/23/12	22		100%
24		Design iteration 2	6 days	Fri 2/24/12	Fri 3/2/12	19		100%
25		Update Kids section homepage	6 days	Fri 2/24/12	Fri 3/2/12			100%
26		Usability testing	22 days	Mon 2/20/12	Tue 3/20/12			100%

Kids.gov Redesign prject schedule

ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
27		Prepare test scripts and find test particpatns	10 days	Mon 2/20/12	Fri 3/2/12	19FF,24FF		100%
28		Perform usability testing	5 days	Mon 3/5/12	Fri 3/9/12	27		100%
29		Analze usability test results and prepare report	5 days	Mon 3/12/12	Fri 3/16/12	28		100%
30		Evaluate usability report for design changes	2 days	Mon 3/19/12	Tue 3/20/12	29		100%
31		Design iteration 3	9 days	Wed 3/21/12	Mon 4/2/12	26,24		100%
32		Design Kids section	8 days	Wed 3/21/12	Fri 3/30/12			100%
33		Design Teens section	8 days	Wed 3/21/12	Fri 3/30/12			100%
34		Design Grown Ups section	8 days	Wed 3/21/12	Fri 3/30/12			100%
35		Design downlevel templates	8 days	Wed 3/21/12	Fri 3/30/12			100%
36		States page	8 days	Wed 3/21/12	Fri 3/30/12			100%
37		Link list page	8 days	Wed 3/21/12	Fri 3/30/12			100%
38		Narrative/Video page	8 days	Wed 3/21/12	Fri 3/30/12			100%
39		Management review	1 day	Mon 4/2/12	Mon 4/2/12	32,33,34,35		100%
40		Implement final design changes	3 days	Tue 4/3/12	Thu 4/5/12	39		100%
41		Content gap completion	106 days	Fri 12/2/11	Fri 4/27/12	5		100%
42		Update Access form to allow entering content gaps	30 days	Fri 12/2/11	Thu 1/12/12			100%
43		Fill in kids audience gaps	11 days	Fri 1/13/12	Fri 1/27/12	42		100%
44		Fill in teens audience gaps	11 days	Fri 1/13/12	Fri 1/27/12	42		100%
45		Fill in teacher audience gaps	20 days	Mon 1/30/12	Fri 2/24/12	44		100%
46		Fill in parent audience gaps	35 days	Mon 3/12/12	Fri 4/27/12	45,28		100%
47		Development	61 days	Wed 3/7/12	Wed 5/30/12			100%
48		HTML/CSS development	24 days	Fri 4/6/12	Wed 5/9/12			100%
49		Create design specifictions and image slices	2 days	Fri 4/6/12	Mon 4/9/12	14		100%
50		Implement baseline template structure	8 days	Tue 4/10/12	Thu 4/19/12	49		100%
51		Implement homepage template	2 days	Fri 4/20/12	Mon 4/23/12	50		100%
52		Implement topic page template	1 day	Tue 4/24/12	Tue 4/24/12	51		100%


Kids.gov Redesign project schedule

ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
53		Implement downlevel page templates	3 days	Wed 4/25/12	Fri 4/27/12	52		100%
54		States page	3 days	Wed 4/25/12	Fri 4/27/12			100%
55		Link list page	3 days	Wed 4/25/12	Fri 4/27/12			100%
56		Narrative/Video page	3 days	Wed 4/25/12	Fri 4/27/12			100%
57		Implement kids skin	1 day	Mon 4/30/12	Mon 4/30/12	53		100%
58		Implement teens skin	1 day	Tue 5/1/12	Tue 5/1/12	57		100%
59		Implement grown-ups skin	1 day	Wed 5/2/12	Wed 5/2/12	58		100%
60		Final accessibility review & template changes	5 days	Thu 5/3/12	Wed 5/9/12	59		100%
61		CMS Implementaiton	61 days	Wed 3/7/12	Wed 5/30/12			100%
62		Installand configure CM 1	28 days	Wed 3/7/12	Fri 4/13/12	13		100%
63		Determine publishing architecture & basic admin training	2 days	Mon 4/16/12	Tue 4/17/12	62		100%
64		Create user accounts for CM 1	2 days	Mon 4/16/12	Tue 4/17/12	62		100%
65		Test baseline install of CM 1	2 days	Wed 4/18/12	Thu 4/19/12	64		100%
66		Decide WCM model in CM 1 based on design	1 day	Fri 4/20/12	Fri 4/20/12	65		100%
67		CM 1 training	2 days	Mon 5/7/12	Tue 5/8/12	48FF-1 day,66		100%
68		Implement templates in CM 1	13 days	Wed 5/9/12	Fri 5/25/12	67,63		100%
69		Baseline template	3 days	Wed 5/9/12	Fri 5/11/12			100%
70		Homepage template	3 days	Mon 5/14/12	Wed 5/16/12	69		100%
71		Topic page template	3 days	Thu 5/17/12	Mon 5/21/12	70		100%
72		Downlevel templates	1 day	Tue 5/22/12	Tue 5/22/12	71		100%
73		States page	1 day	Tue 5/22/12	Tue 5/22/12			100%
74		Link list page	1 day	Tue 5/22/12	Tue 5/22/12			100%
75		Narrative/Video page	1 day	Tue 5/22/12	Tue 5/22/12			100%
76		3 audience skins	3 days	Wed 5/23/12	Fri 5/25/12	72		100%
77		Test templates in CM 1	3 days	Mon 5/28/12	Wed 5/30/12	76		100%
78		Test kids templates	1 day	Mon 5/28/12	Mon 5/28/12			100%
79		Test teens templates	1 day	Tue 5/29/12	Tue 5/29/12	78		100%

Kids.gov Redesign project schedule

ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
80		Test grown up templates	1 day	Wed 5/30/12	Wed 5/30/12	79		100%
81		Content migration	50 days	Fri 4/6/12	Thu 6/14/12			100%
82		Determine content migration report requirements	1 day	Mon 4/30/12	Mon 4/30/12	41		100%
83		Generate Access report will all content to be migrated	5 days	Tue 5/1/12	Mon 5/7/12	82		100%
84		Content migration training	1 day	Thu 5/31/12	Thu 5/31/12	83,61		100%
85		Create images	20 days	Fri 4/6/12	Thu 5/3/12	18,41FF-5 days		100%
86		Perform content migration	5 days	Fri 6/1/12	Thu 6/7/12	84,85		100%
87		Migrate pages 1 - 25	5 days	Fri 6/1/12	Thu 6/7/12			100%
88		Migrate pages 26-50	5 days	Fri 6/1/12	Thu 6/7/12			100%
89		Migrate pages 51-75	5 days	Fri 6/1/12	Thu 6/7/12			100%
90		Migrate pages 76-100	5 days	Fri 6/1/12	Thu 6/7/12			100%
91		Migrate pages 101-125	5 days	Fri 6/1/12	Thu 6/7/12			100%
92		Migrate pages 126-150	5 days	Fri 6/1/12	Thu 6/7/12			100%
93		Migrate pages 151-175	5 days	Fri 6/1/12	Thu 6/7/12			100%
94		Migrate pages 176-200	5 days	Fri 6/1/12	Thu 6/7/12			100%
95		Final content QA	5 days	Fri 6/8/12	Thu 6/14/12	86		100%
96		Announce new design on current site	1 day	Tue 5/8/12	Tue 5/8/12	103SS-30 days		100%
97		Deployment	7 days	Fri 6/8/12	Mon 6/18/12			100%
98		Verify published site	2 days	Wed 6/13/12	Thu 6/14/12	81FF		100%
99		Create redirect list from old site to new (kids.usa.gov)	1 day	Fri 6/15/12	Fri 6/15/12	98		100%
100		Configure Akamai	5 days	Fri 6/8/12	Thu 6/14/12	81FF		100%
101		Add DNS entry for kids.usa.gov	1 day	Fri 6/15/12	Fri 6/15/12	98,100		100%
102		Implement redirects from kids.gov to kids.usa.gov	1 day	Mon 6/18/12	Mon 6/18/12	101		100%
103		Launch	0 days	Mon 6/18/12	Mon 6/18/12	102		100%

Kids.gov Redesign project schedule

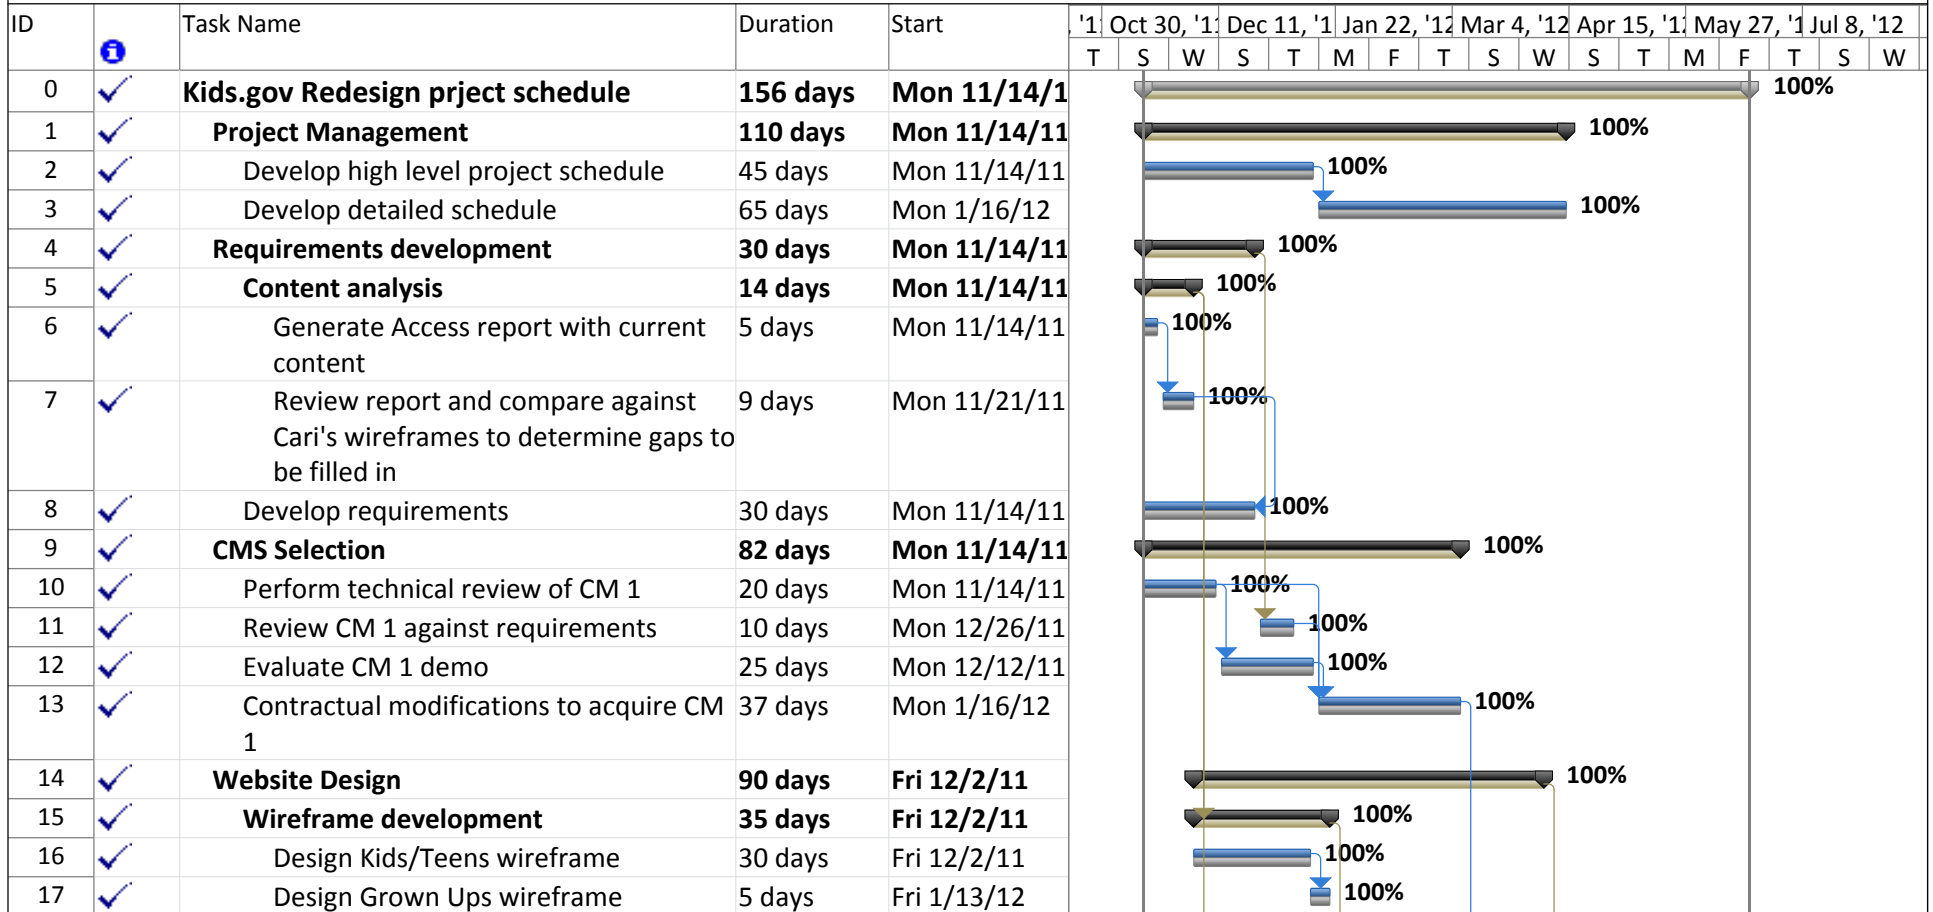

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


Kids.gov Redesign project schedule

ID		Task Name	Duration	Start	'1	Oct 30, '1	Dec 11, '1	Jan 22, '12	Mar 4, '12	Apr 15, '12	May 27, '12	Jul 8, '12				
					T	S	W	S	T	M	F	T	S	W	S	T
18		Design development	55 days	Fri 1/20/12												
19		Design iteration 1	25 days	Fri 1/20/12												
20		Design Kids section	18 days	Fri 1/20/12												
21		Design Teens section	3 days	Wed 2/15/12												
22		Design Grown Ups section	3 days	Mon 2/20/12												
23		Management review	1 day	Thu 2/23/12												
24		Design iteration 2	6 days	Fri 2/24/12												
25		Update Kids section homepage	6 days	Fri 2/24/12												
26		Usability testing	22 days	Mon 2/20/12												
27		Prepare test scripts and find test particpatns	10 days	Mon 2/20/12												
28		Perform usability testing	5 days	Mon 3/5/12												
29		Analze usability test results and prepare report	5 days	Mon 3/12/12												
30		Evaluate usability report for design changes	2 days	Mon 3/19/12												
31		Design iteration 3	9 days	Wed 3/21/12												
32		Design Kids section	8 days	Wed 3/21/12												
33		Design Teens section	8 days	Wed 3/21/12												
34		Design Grown Ups section	8 days	Wed 3/21/12												
35		Design downlevel templates	8 days	Wed 3/21/12												
36		States page	8 days	Wed 3/21/12												

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


Kids.gov Redesign project schedule

ID		Task Name	Duration	Start	'11	Oct 30, '11	Nov 10, '11	Dec 11, '11	Jan 22, '12	Jan 29, '12	Feb 5, '12	Feb 12, '12	Mar 4, '12	Mar 11, '12	Apr 15, '12	May 27, '12	Jun 10, '12	Jul 8, '12
					T	S	W	S	T	M	F	T	S	W	S	T	M	F
37		Link list page	8 days	Wed 3/21/12											100%			
38		Narrative/Video page	8 days	Wed 3/21/12											100%			
39		Management review	1 day	Mon 4/2/12											100%			
40		Implement final design changes	3 days	Tue 4/3/12											100%			
41		Content gap completion	106 days	Fri 12/2/11												100%		
42		Update Access form to allow entering content gaps	30 days	Fri 12/2/11														
43		Fill in kids audience gaps	11 days	Fri 1/13/12														
44		Fill in teens audience gaps	11 days	Fri 1/13/12														
45		Fill in teacher audience gaps	20 days	Mon 1/30/12														
46		Fill in parent audience gaps	35 days	Mon 3/12/12														
47		Development	61 days	Wed 3/7/12														
48		HTML/CSS development	24 days	Fri 4/6/12														
49		Create design specifictions and image slices	2 days	Fri 4/6/12														
50		Implement baseline template structure	8 days	Tue 4/10/12														
51		Implement homepage template	2 days	Fri 4/20/12														
52		Implement topic page template	1 day	Tue 4/24/12														
53		Implement downlevel page templates	3 days	Wed 4/25/12														
54		States page	3 days	Wed 4/25/12														

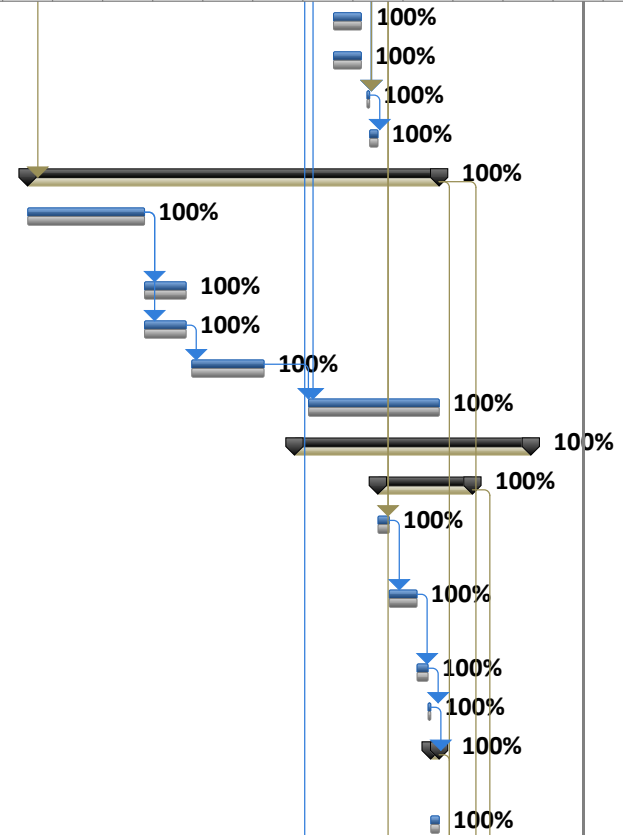


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


Kids.gov Redesign project schedule

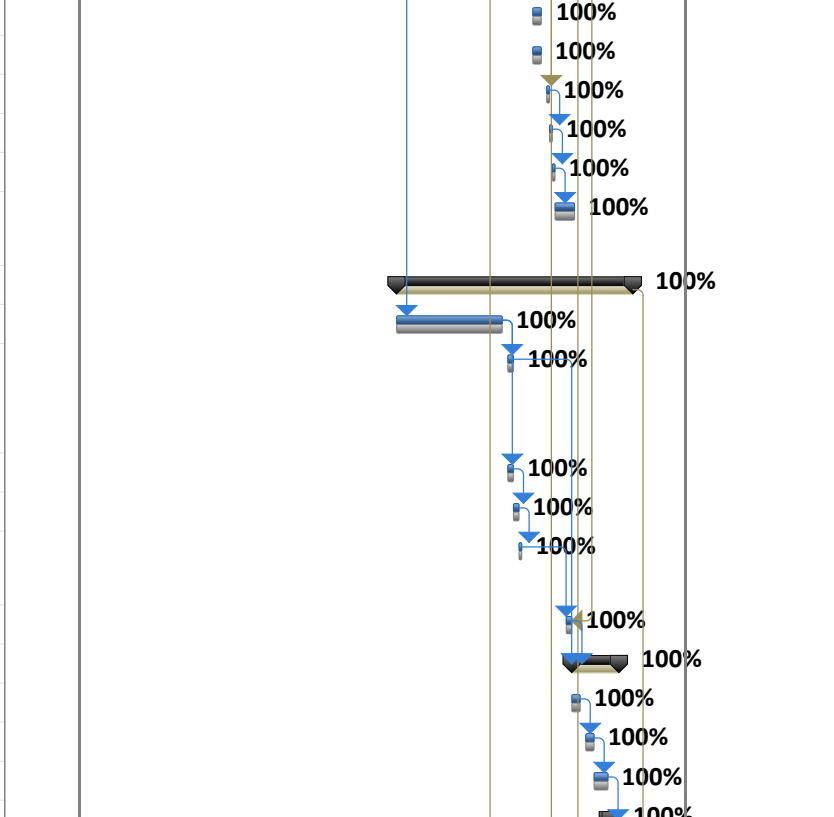ID		Task Name	Duration	Start	'1	Oct 30, '1	1	Dec 11, '1	1	Jan 22, '12	1	Mar 4, '12	1	Apr 15, '12	1	May 27, '12	1	Jul 8, '12	
					T	S	W	S	T	M	F	T	S	W	S	T	M	F	T
55		Link list page	3 days	Wed 4/25/12															
56		Narrative/Video page	3 days	Wed 4/25/12															
57		Implement kids skin	1 day	Mon 4/30/12															
58		Implement teens skin	1 day	Tue 5/1/12															
59		Implement grown-ups skin	1 day	Wed 5/2/12															
60		Final accessibility review & template changes	5 days	Thu 5/3/12															
61		CMS Implementaiton	61 days	Wed 3/7/12															
62		Installand configure CM 1	28 days	Wed 3/7/12															
63		Determine publishing architecture & basic admin training	2 days	Mon 4/16/12															
64		Create user accounts for CM 1	2 days	Mon 4/16/12															
65		Test baseline install of CM 1	2 days	Wed 4/18/12															
66		Decide WCM model in CM 1 based on design	1 day	Fri 4/20/12															
67		CM 1 training	2 days	Mon 5/7/12															
68		Implement templates in CM 1	13 days	Wed 5/9/12															
69		Baseline template	3 days	Wed 5/9/12															
70		Homepage template	3 days	Mon 5/14/12															
71		Topic page template	3 days	Thu 5/17/12															
72		Downlevel templates	1 day	Tue 5/22/12															

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


Kids.gov Redesign project schedule

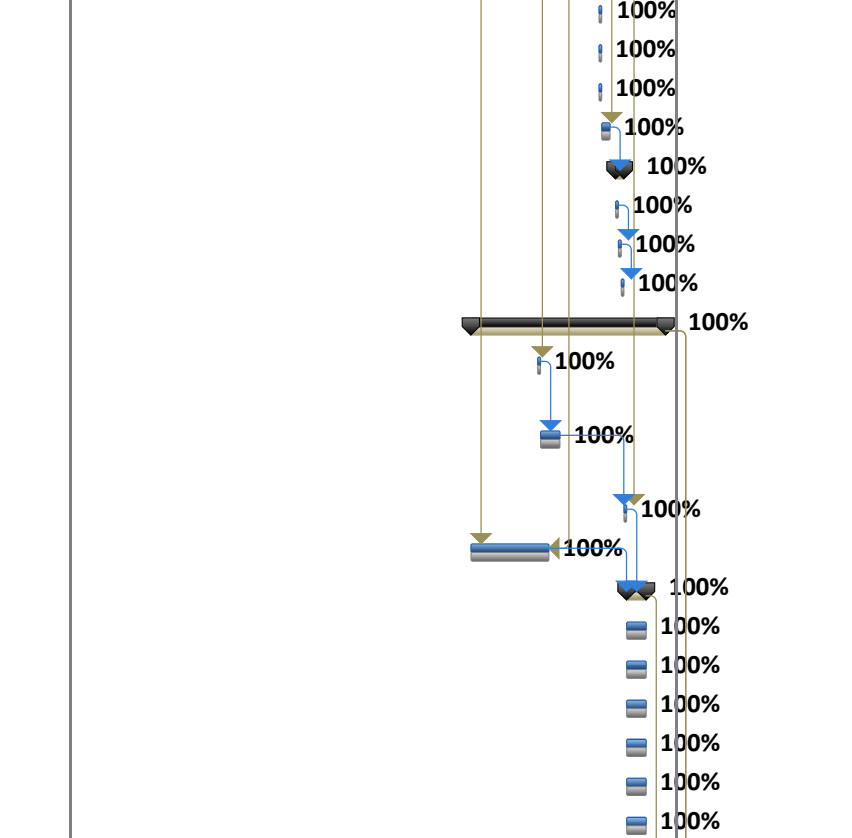
ID		Task Name	Duration	Start	'1 Oct 30, '11 Dec 11, '11 Jan 22, '12 Mar 4, '12 Apr 15, '12 May 27, '12 Jul 8, '12														
					T	S	W	S	T	M	F	T	S	W	S	T	M	F	T
73		States page	1 day	Tue 5/22/12															
74		Link list page	1 day	Tue 5/22/12															
75		Narrative/Video page	1 day	Tue 5/22/12															
76		3 audience skins	3 days	Wed 5/23/12															
77		Test templates in CM 1	3 days	Mon 5/28/12															
78		Test kids templates	1 day	Mon 5/28/12															
79		Test teens templates	1 day	Tue 5/29/12															
80		Test grown up templates	1 day	Wed 5/30/12															
81		Content migration	50 days	Fri 4/6/12															
82		Determine content migration report requirements	1 day	Mon 4/30/12															
83		Generate Access report will all content to be migrated	5 days	Tue 5/1/12															
84		Content migration training	1 day	Thu 5/31/12															
85		Create images	20 days	Fri 4/6/12															
86		Perform content migration	5 days	Fri 6/1/12															
87		Migate pages 1 - 25	5 days	Fri 6/1/12															
88		Migrate pages 26-50	5 days	Fri 6/1/12															
89		Migrate pages 51-75	5 days	Fri 6/1/12															
90		Migrate pages 76-100	5 days	Fri 6/1/12															
91		Migrate pages 101-125	5 days	Fri 6/1/12															
92		Migrate pages 126-150	5 days	Fri 6/1/12															

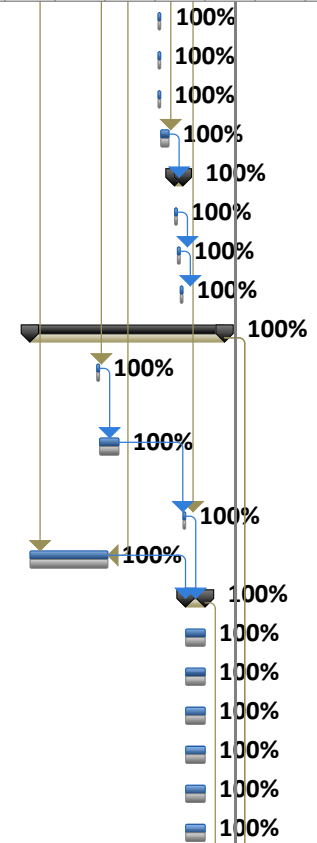

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Kids.gov Redesign project schedule

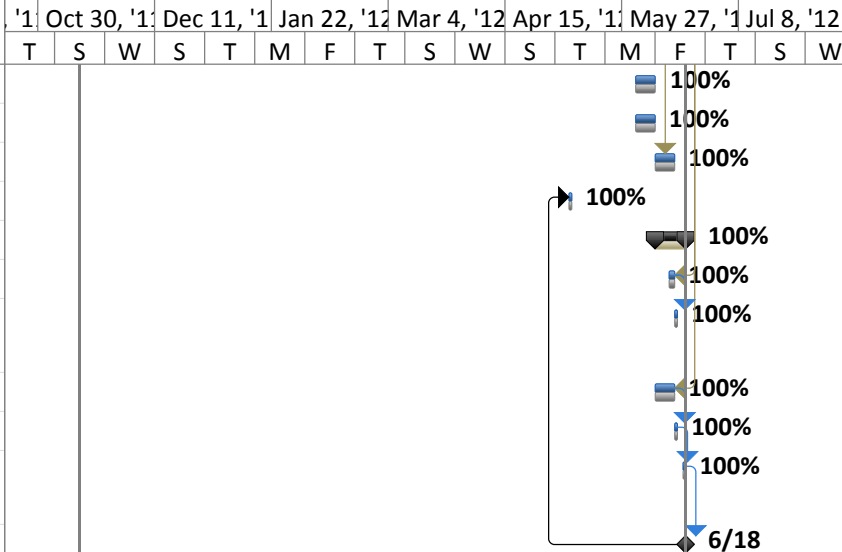ID		Task Name	Duration	Start																												
					'1	Oct 30, '1	'1	Dec 11, '1	'1	Jan 22, '12	'12	Mar 4, '12	'12	Apr 15, '1	'12	May 27, '1	'12	Jul 8, '12	'12													
					T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W				
93		Migrate pages 151-175	5 days	Fri 6/1/12																												
94		Migrate pages 176-200	5 days	Fri 6/1/12																												
95		Final content QA	5 days	Fri 6/8/12																												
96		Announce new design on current site	1 day	Tue 5/8/12																												
97		Deployment	7 days	Fri 6/8/12																												
98		Verify published site	2 days	Wed 6/13/12																												
99		Create redirect list from old site to new (kids.usa.gov)	1 day	Fri 6/15/12																												
100		Configure Akamai	5 days	Fri 6/8/12																												
101		Add DNS entry for kids.usa.gov	1 day	Fri 6/15/12																												
102		Implement redirects from kids.gov to kids.usa.gov	1 day	Mon 6/18/12																												
103		Launch	0 days	Mon 6/18/12																												

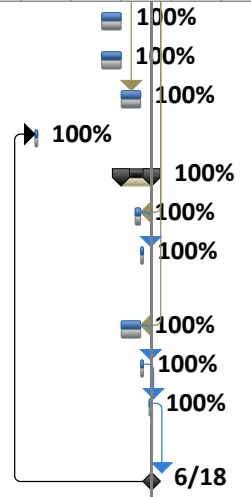

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	
